



VENICE DUAL FORCE MAIN SEWER PROJECT

Updated Schedule: Project Completion - Spring 2021

Below is the projected schedule for our various work sites. Our project has been extended by a few months and the dates below reflect our most current timeline of activities. The completion dates include restoration work that will be performed at each location.

Anticipated completion dates by location:

Venice

- 11/6/2019 Hurricane Street at Canal Court
- 8/21/2020 Marquesas Way at Via Dolce

Marina del Rey

- 7/19/2020 Via Marina at Marquesas Way
- 7/9/2020 Via Marina at Tahiti Way
- 12/6/2020 Via Marina at Northwest Passage
- 1/7/2021 County Beach Lot #13 along Via Marina at Old Harbor Lane


Playa del Rey

- 1/8/2021 Pacific Avenue at 62nd Avenue;
- 9/10/2020 Pacific Avenue between Convoy Street and Culver Boulevard
- 2/5/2021 Pacific Avenue at Vista del Mar
- 1/29/2021 Vista del Mar at Waterview Street

* Schedule is subject to change due to weather and other unforeseen circumstances

VDFM SEWER PROJECT OUTREACH CONTACT

Tonya Durrell at (213) 485-3221 or Tonya.Durrell@lacity.org
 Josh Melendez at (213) 485-3221 or Joshua.Melendez@lacity.org
 Danielle Sevilla at (213) 485-3221 or Danielle.Sevilla@lacity.org
 After 5:00 p.m. and weekends, LA Sanitation & Environment
 Customer Care Center: **(800) 773-2489**
 Facebook: www.facebook.com/lacitysan/
 Website: www.lacitysan.org/vdfm

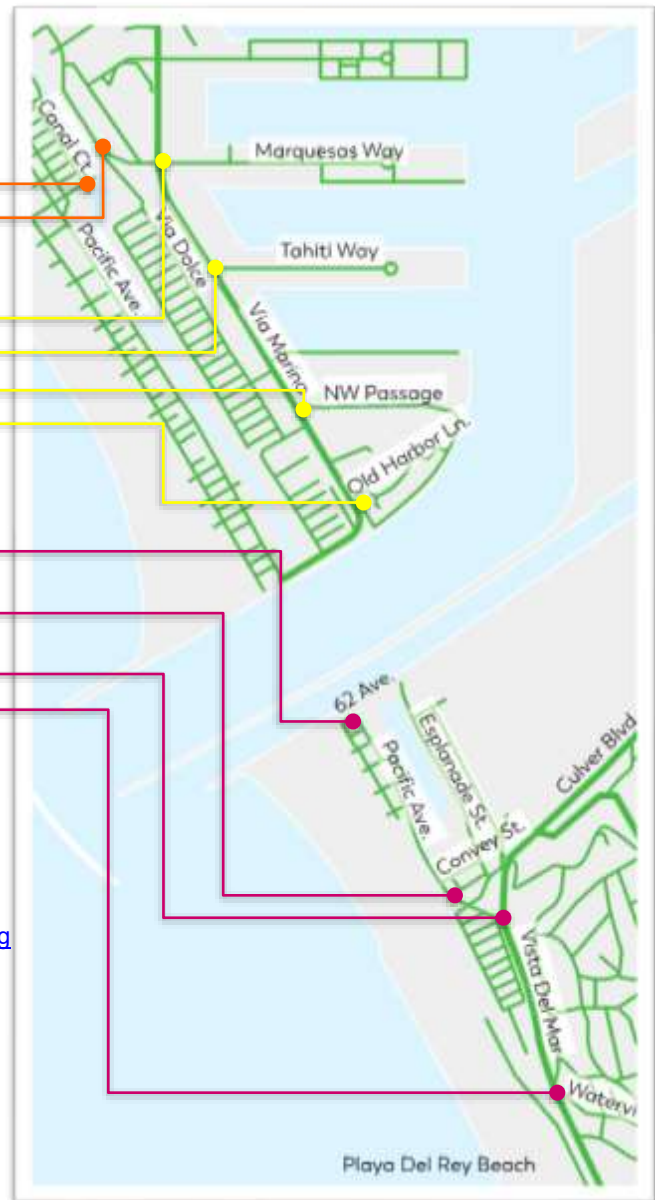



VENICE DUAL FORCE MAIN SEWER PROJECT

Completed Construction & Anticipated Restoration Dates

Shaft Construction:

- Construction of all shafts (access points) for the project has been completed at this time; this includes all project locations in Venice, Marina del Rey, and Playa del Rey
- Access points are constructed to allow for lowering and launching of the micro tunnel boring machine which creates the tunnel for installation of the sewer pipe segments

Tunneling and Sewer Pipe Installation:

- Micro tunneling and installation of sewer pipe segments has been completed at the following shaft locations:
- **Shaft 1-2:** Shaft 1 (Pacific Avenue at Vista del Mar) to Shaft 2 (Pacific Avenue at Culver Boulevard/Convoy Street)
- **Shaft 4-5:** Shaft 4 (Pacific Avenue at 62nd Avenue) to Shaft 5 (County Beach Parking Lot #13 along Via Marina at Old Harbor Lane)
- **Shaft 5-6:** Shaft 5 (County Beach Parking Lot #13 along Via Marina at Old Harbor Lane) to Shaft 6 (Via Marina at Northwest Passage)
- **Shaft 6-8:** Shaft 6 (Via Marina at Northwest Passage) to Shaft 8 (Via Marina at Tahiti Way)
- **Shaft 9-10:** Shaft 9 (Via Marina at Marquesas Way) to Shaft 10 (Marquesas Way at Via Dolce)
- **Shaft 10-11:** Shaft 10 (Marquesas Way at Via Dolce) to Shaft 11 (Hurricane Street at Canal Court)

At the above noted locations while shaft construction, tunneling, and pipe installation is finished, crews are still conducting tasks related to fully completing these pipeline segments.

Venice Pumping Plant Generator Replacement Project:

- Remaining activities will mainly occur within the plant, with the exception of some deliveries and demobilization activities

Projected Restoration Start Dates:

- *The following dates are specifically related to restoration work for each shaft site. Part of our restoration efforts will involve the removal of sound walls.*
- *Coordination of restoration may require a pause between the conclusion of construction activities and the commencement of restoration tasks*
- **Marquesas Way at Via Dolce:** 8/1/2020
- **Via Marina at Marquesas Way:** 7/8/2020
- **Via Marina at Tahiti Way:** 7/6/2020
- **Via Marina at Northwest Passage:** 11/23/2020
- **County Beach Parking Lot #13 along Via Marina at Old Harbor Lane:** 12/14/2020
While shaft area restoration will occur, this location will continue to be utilized for construction office space and staging
- **Pacific Avenue at 62nd Avenue:** 12/29/2020
- **Pacific Avenue at Culver Boulevard/Convoy Street:** 8/24/2020
- **Pacific Avenue at Vista del Mar:** 1/21/2021
- **Vista del Mar at Waterview Street:** 1/11/2021

